M. A. R. 57 (Rule 116)

Measurement Book

No. B

AGE/KSOL/SBA/000027 dt. 05/03/18

567558

I st & Final bill

Final No. .....

Name of Work ..... From ..... To .....

Name of Contractor of nature of Agency ..... M/S. KRIDL .....

Date of commencement of work .....

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
	2	3	4	5	6	7	8
	Name of work :- Development of Pipeline park mallasandra in ward No. 13						
	WO # BBMP/EE/DD/WO/115/2017-18, 21-06-17.						
	Job code :- 013-17-000059						
	A.A :- JC/D/AS/PR/22/16-17, Dt :- 05-06-2017.						
	T.S :- CE/DZ/TS/62/16-17, Dt :- 12-06-2017.						
	Agr :- EE/DD/Agr/115/2017-18 Dt :- 21-06-2017.						
	Est Cost :- Rs. 50.00 Lakhs.						

Scanned by CamScanner

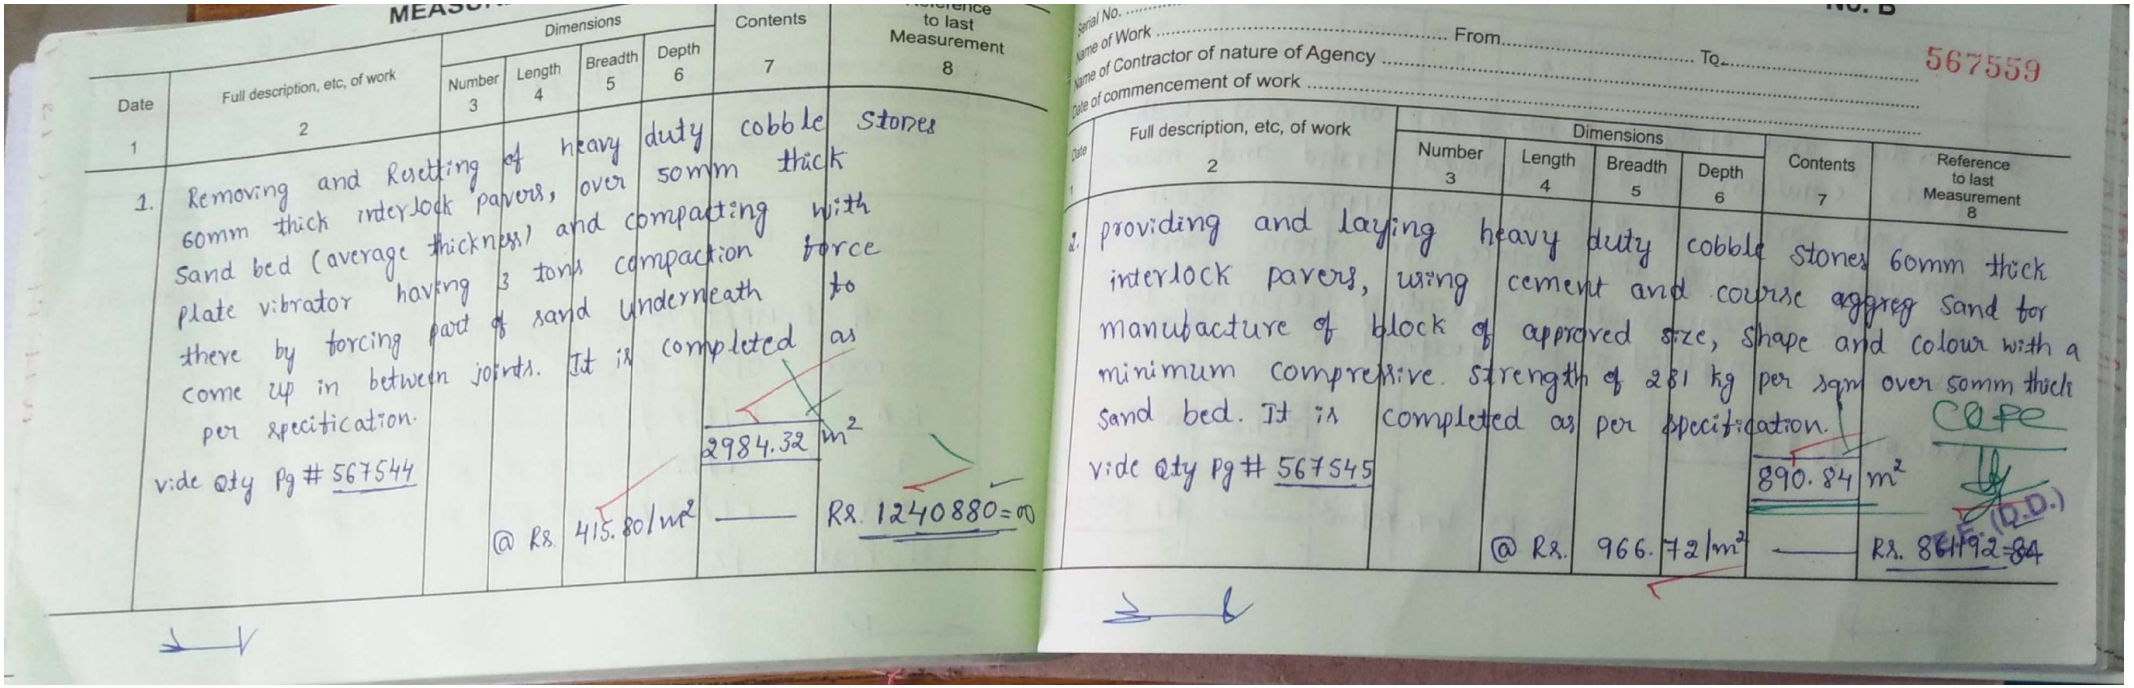

MEASU...

Date	Full description, etc, of work	Dimensions: Number	Length	Breadth	Depth	Contents	Reference to last Measurement
1	2	3	4	5	6	7	8
1.	Removing and Resetting of heavy duty cobble Stones 60mm thick interlock pavers, over 50mm thick Sand bed (average thickness) and compacting with plate vibrator having 3 tons compaction force there by forcing part of sand underneath to come up in between joints. It is completed as per specification. vide Qty Pg # 567544					2984.32 m^2	@ Rs. 415.80/m^2 — Rs. 1240880=00

Serial No. .....
Name of Work ..... From ..... To .....
Name of Contractor of nature of Agency .....
Date of commencement of work .....

567559

Date	Full description, etc, of work	Dimensions: Number	Length	Breadth	Depth	Contents	Reference to last Measurement
1	2	3	4	5	6	7	8
2.	providing and laying heavy duty cobble stones 60mm thick interlock pavers, using cement and course aggreg Sand for manufacture of block of approved size, shape and colour with a minimum compressive strength of 281 kg per sqm over 50mm thick sand bed. It is completed as per specification. vide Qty Pg # 567545					890.84 m^2	@ Rs. 966.72/m^2 — Rs. 861192=84

COPE (D.D.)

Scanned by CamScanner

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
1	2	Number 3	Length 4	Breadth 5	Depth 6	7	8
12.	Supplying and fixing precast reinforced concrete slab 25cm thick including cost of reinforcement as per design and drawing material cost, transportation, hire charges of machinery, machine cutting the vertical face to get plain even surface. It is completed as per specification. vide qty pg# 567553					51.20 m^2	C&PC Rs. 262400=00
						@ Rs. 5125.00/m^2	
13.	Earthwork excavation for foundation of buildings, water supply, Sanitary lines and electrical conduits either in pits or in trenches 1.5m and above in width, in ordinary						

Serial No. .....
Name of Work ..... From..... To.....
Name of Contractor of nature of Agency .....
Date of commencement of work .....

Measurement Book No. B

567564

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
1	2	Number 3	Length 4	Breadth 5	Depth 6	7	8
	Soil not exceeding 1.5m in depth including dressing the bottom and sides of pits & trenches. It is completed as per specification. vide qty pg # 567549					1037.10 m^3	C&PC Rs. 311109=00
						@ Rs. 299.98/m^3	
14.	providing and fixing to wall, ceiling and floor high density polyethylene pipes 6.00 kgf/sq cm working pressure 63 mm outside diameter raising mains & exposed distribution pipes with						

Scanned by CamScanner

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	Audited and admitted for Rs. 4999760=00 4578181=00 — — 421579=00 Passed by Chargeable for Rs. ( ) by a/c Accounts Asst. Exe. Engineer P Dasarahalli Division				Total —		Rs. 4586931=00
					Add 9% KRIDL charges —		(+) 412824=00
					Grand Total —		Rs. 4,99,7 50 =00
	Certificate :- Certified that the work is executed Satisfactorily. 24/05/18 EXECUTIVE ENGINEER-4 KRIDL, BBMP DIVISION BENGALURU-560 010						

Scanned by CamScanner
